








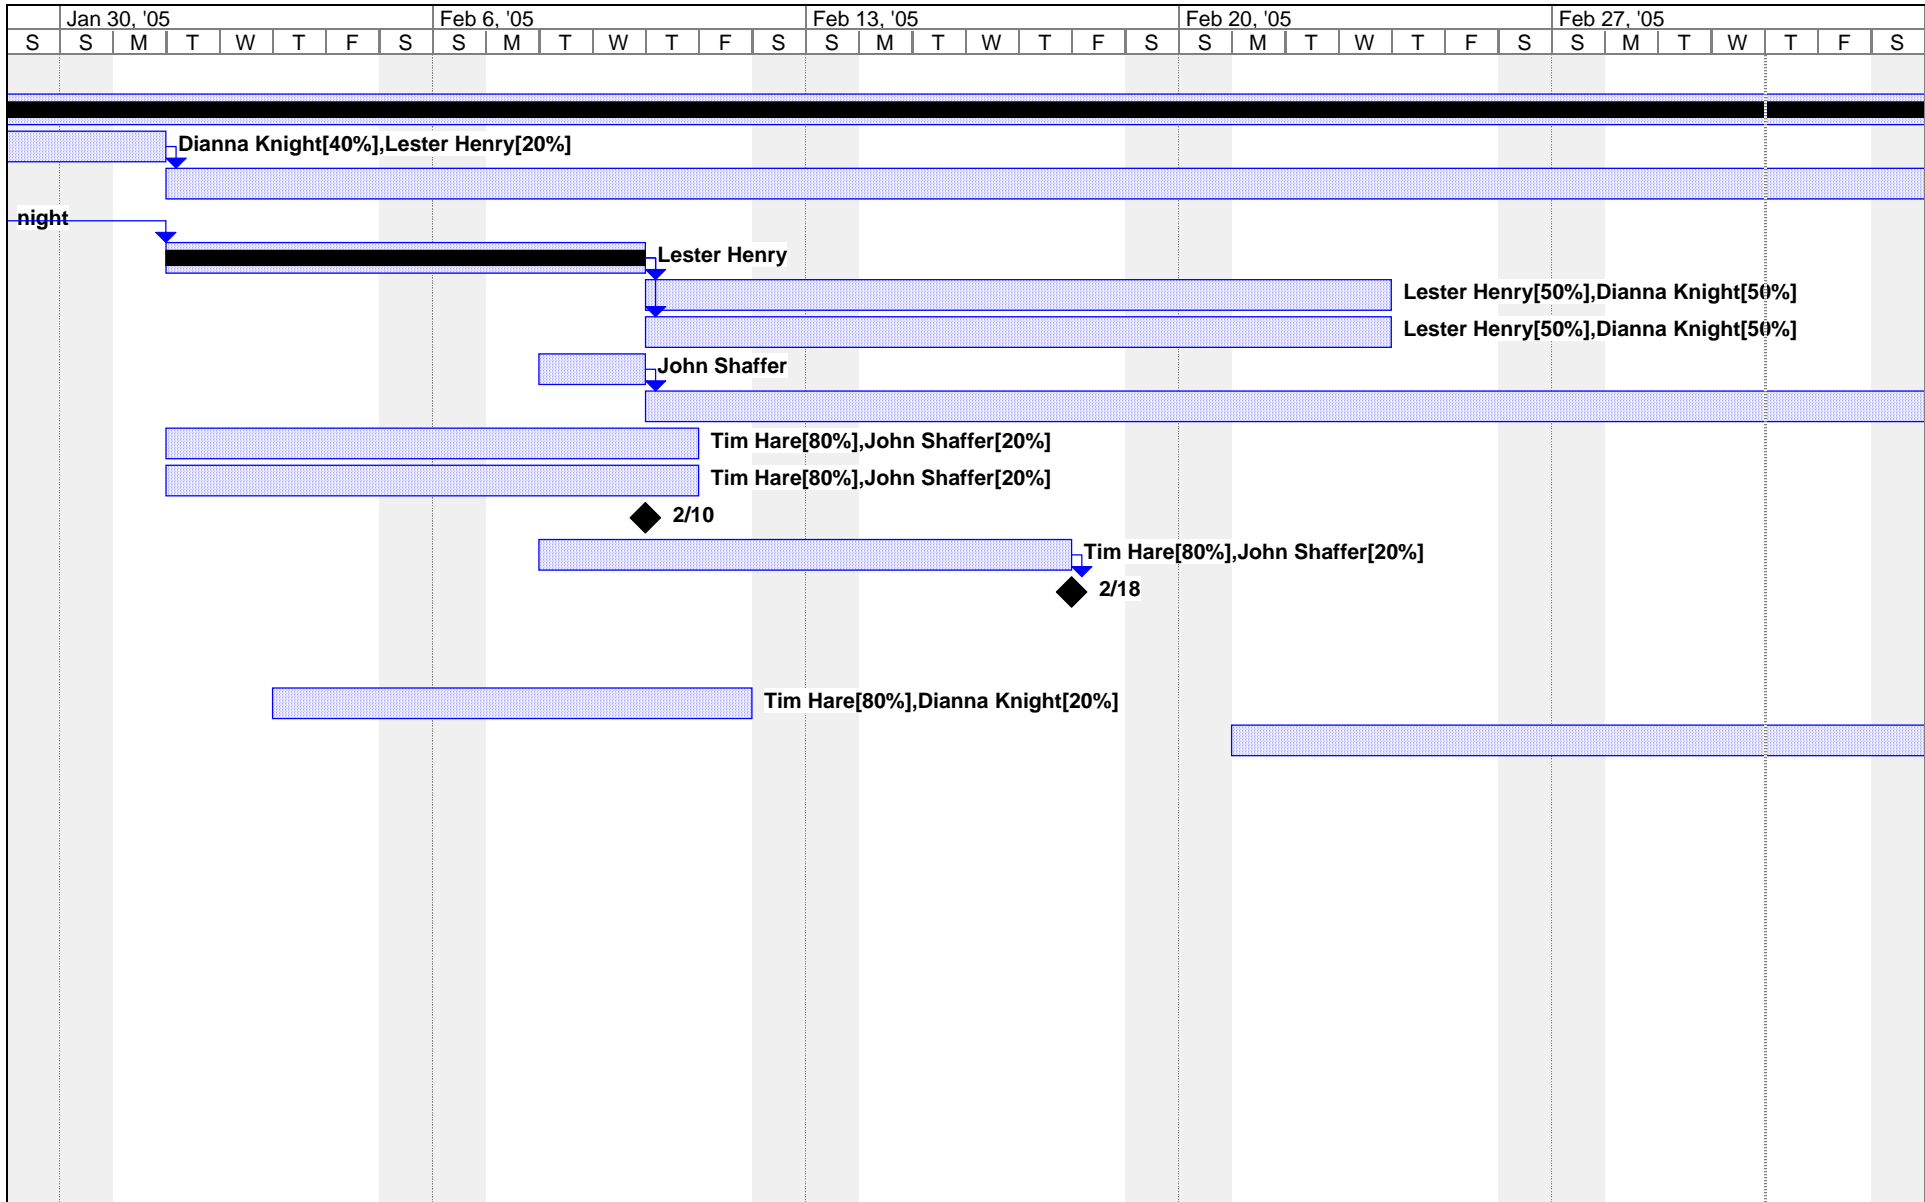
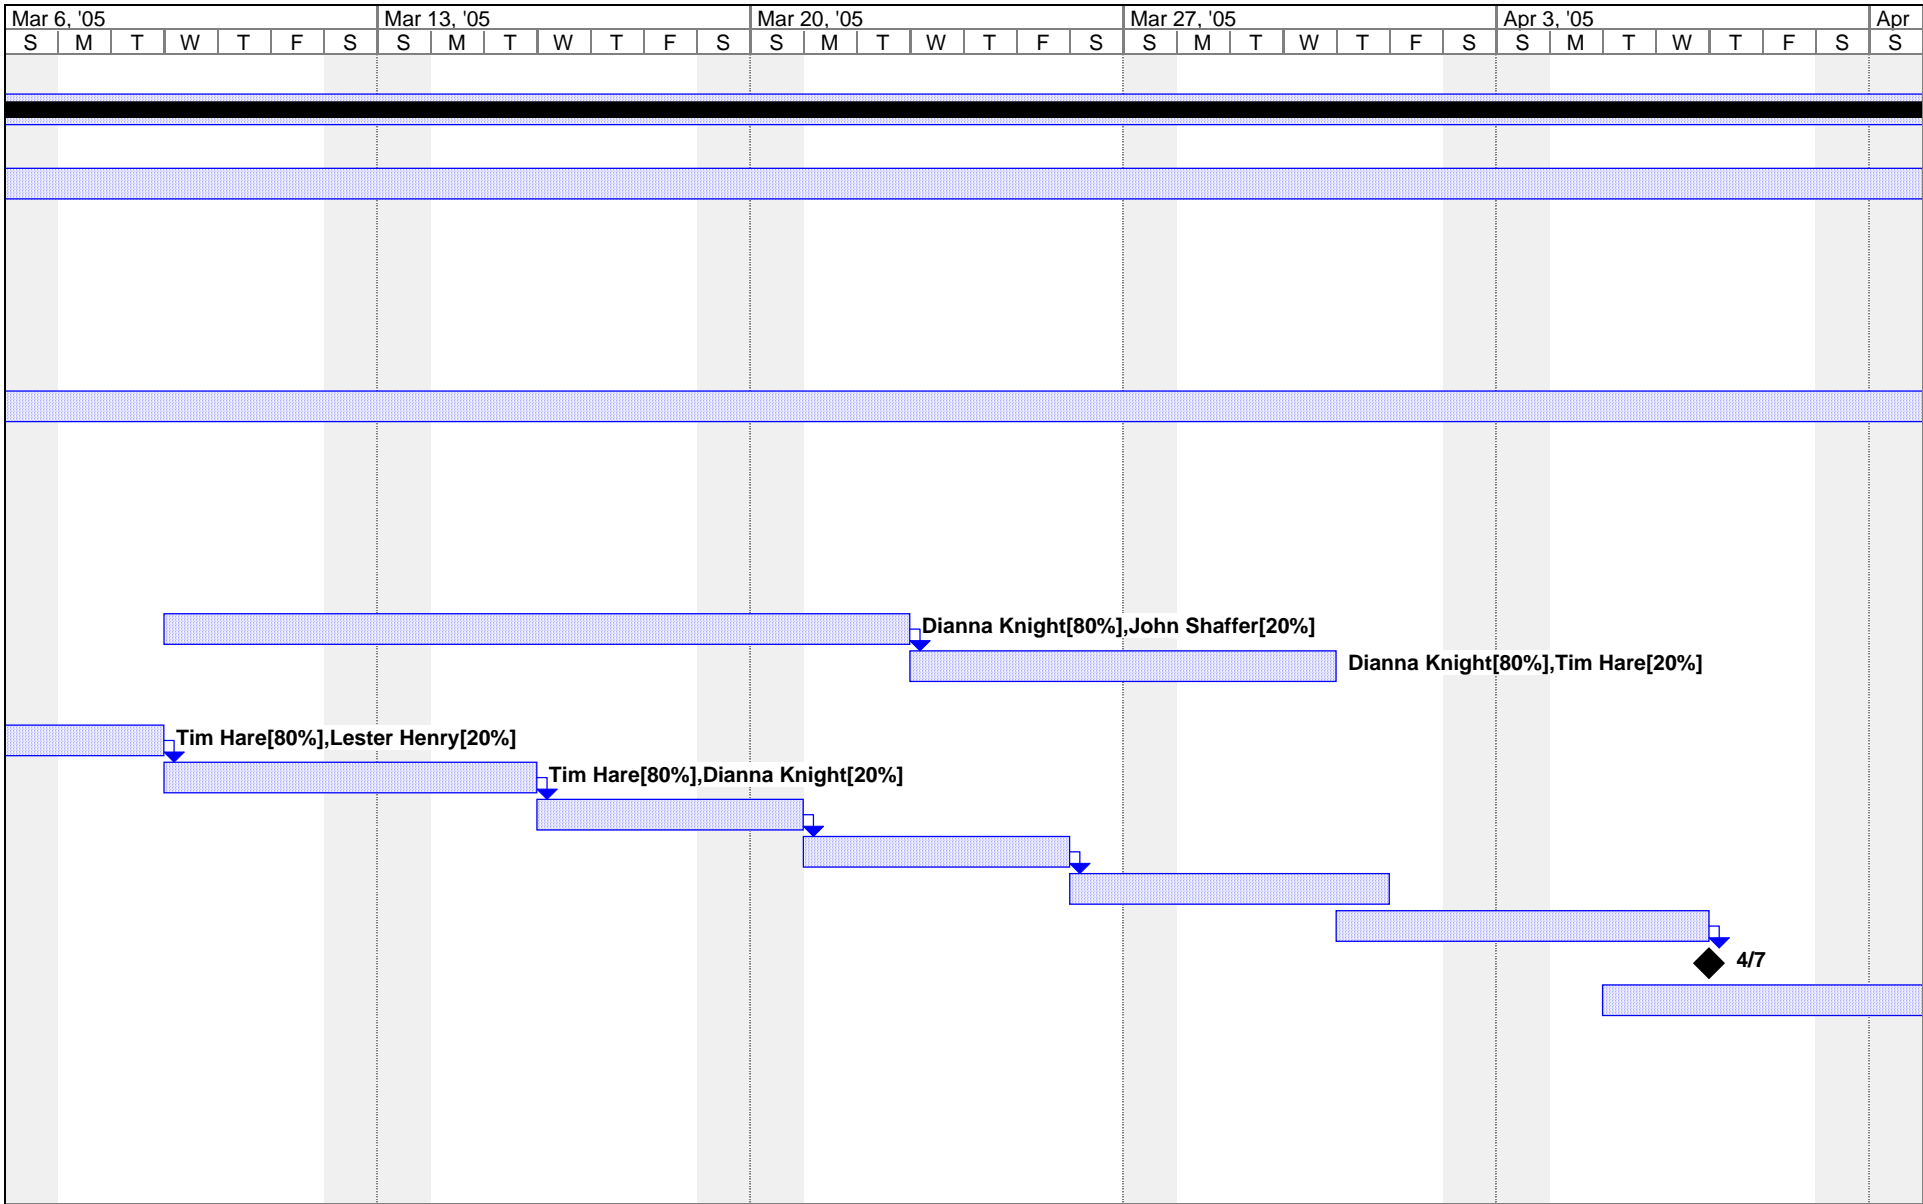


ID	Task Name	Duration	Start	Finish	Predecessors	6, '05							Jan 23, '05							
						M	T	W	T	F	S	S	M	T	W	T	F			
1	Initiating	2 days	Tue 1/18/05	Wed 1/19/05																
2	Project Meetings	74 days	Tue 1/18/05	Thu 4/28/05																
3	Web Interface Development	8 days	Thu 1/20/05	Mon 1/31/05																
4	Project Document Updates	63 days	Tue 2/1/05	Wed 4/27/05	3															
5	Develop Work Breakdown	2 days	Tue 1/25/05	Wed 1/26/05																
6	Create Object Models	7 days	Tue 2/1/05	Wed 2/9/05	5															
7	Prepare Project Plan	10 days	Thu 2/10/05	Wed 2/23/05	6															
8	Prepare Requirements Document	10 days	Thu 2/10/05	Wed 2/23/05	6															
9	Develop Quality Control	2 days	Tue 2/8/05	Wed 2/9/05																
10	White box Testing	45 days	Thu 2/10/05	Tue 4/12/05	9															
11	Determine Data Delivery Structure	8 days	Tue 2/1/05	Thu 2/10/05																
12	Determine Type of Synchronization	8 days	Tue 2/1/05	Thu 2/10/05																
13	Client Approval for Data Delivery System	1 day?	Thu 2/10/05	Thu 2/10/05																
14	Develop Software Interface	8 days	Tue 2/8/05	Thu 2/17/05																
15	Client Approval for Interface	1 day	Fri 2/18/05	Fri 2/18/05	14															
16	Develop Sync System	10 days?	Wed 3/9/05	Tue 3/22/05																
17	Test Hot Sync incorporate into project	7 days?	Wed 3/23/05	Wed 3/30/05	16															
18	Build Supervisor/Job Code Selection	7 days	Thu 2/3/05	Fri 2/11/05																
19	Implement Main Interface	12 days	Mon 2/21/05	Tue 3/8/05																
20	Job Information Entry Screen	5 days	Wed 3/9/05	Tue 3/15/05	19															
21	Add New Job Information	3 days?	Wed 3/16/05	Sun 3/20/05	20															
22	Edit Job Information	5 days?	Mon 3/21/05	Fri 3/25/05	21															
23	Query Timesheet Information	5 days?	Sat 3/26/05	Thu 3/31/05	22															
24	Edit Time sheet Info	5 days?	Thu 3/31/05	Wed 4/6/05																
25	Project Mid Demo	1 day?	Thu 4/7/05	Thu 4/7/05	24															
26	Entry Auditors Travel	5 days?	Tue 4/5/05	Mon 4/11/05																
27	Query Time Sheet Info	4 days?	Tue 4/12/05	Fri 4/15/05	26															
28	Build Timesheet Interface	14 days	Mon 4/18/05	Thu 5/5/05	27															
29	Black box Testing	10 days	Wed 4/13/05	Tue 4/26/05	10															
30	Program Delivery	1 day?	Mon 5/2/05	Mon 5/2/05	29															
31	Project Presentation	1 day?	Tue 5/3/05	Tue 5/3/05																


Project: GeorgiaPalm Date: Thu 3/3/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: GeorgiaPalm Date: Thu 3/3/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	



Project: GeorgiaPalm Date: Thu 3/3/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

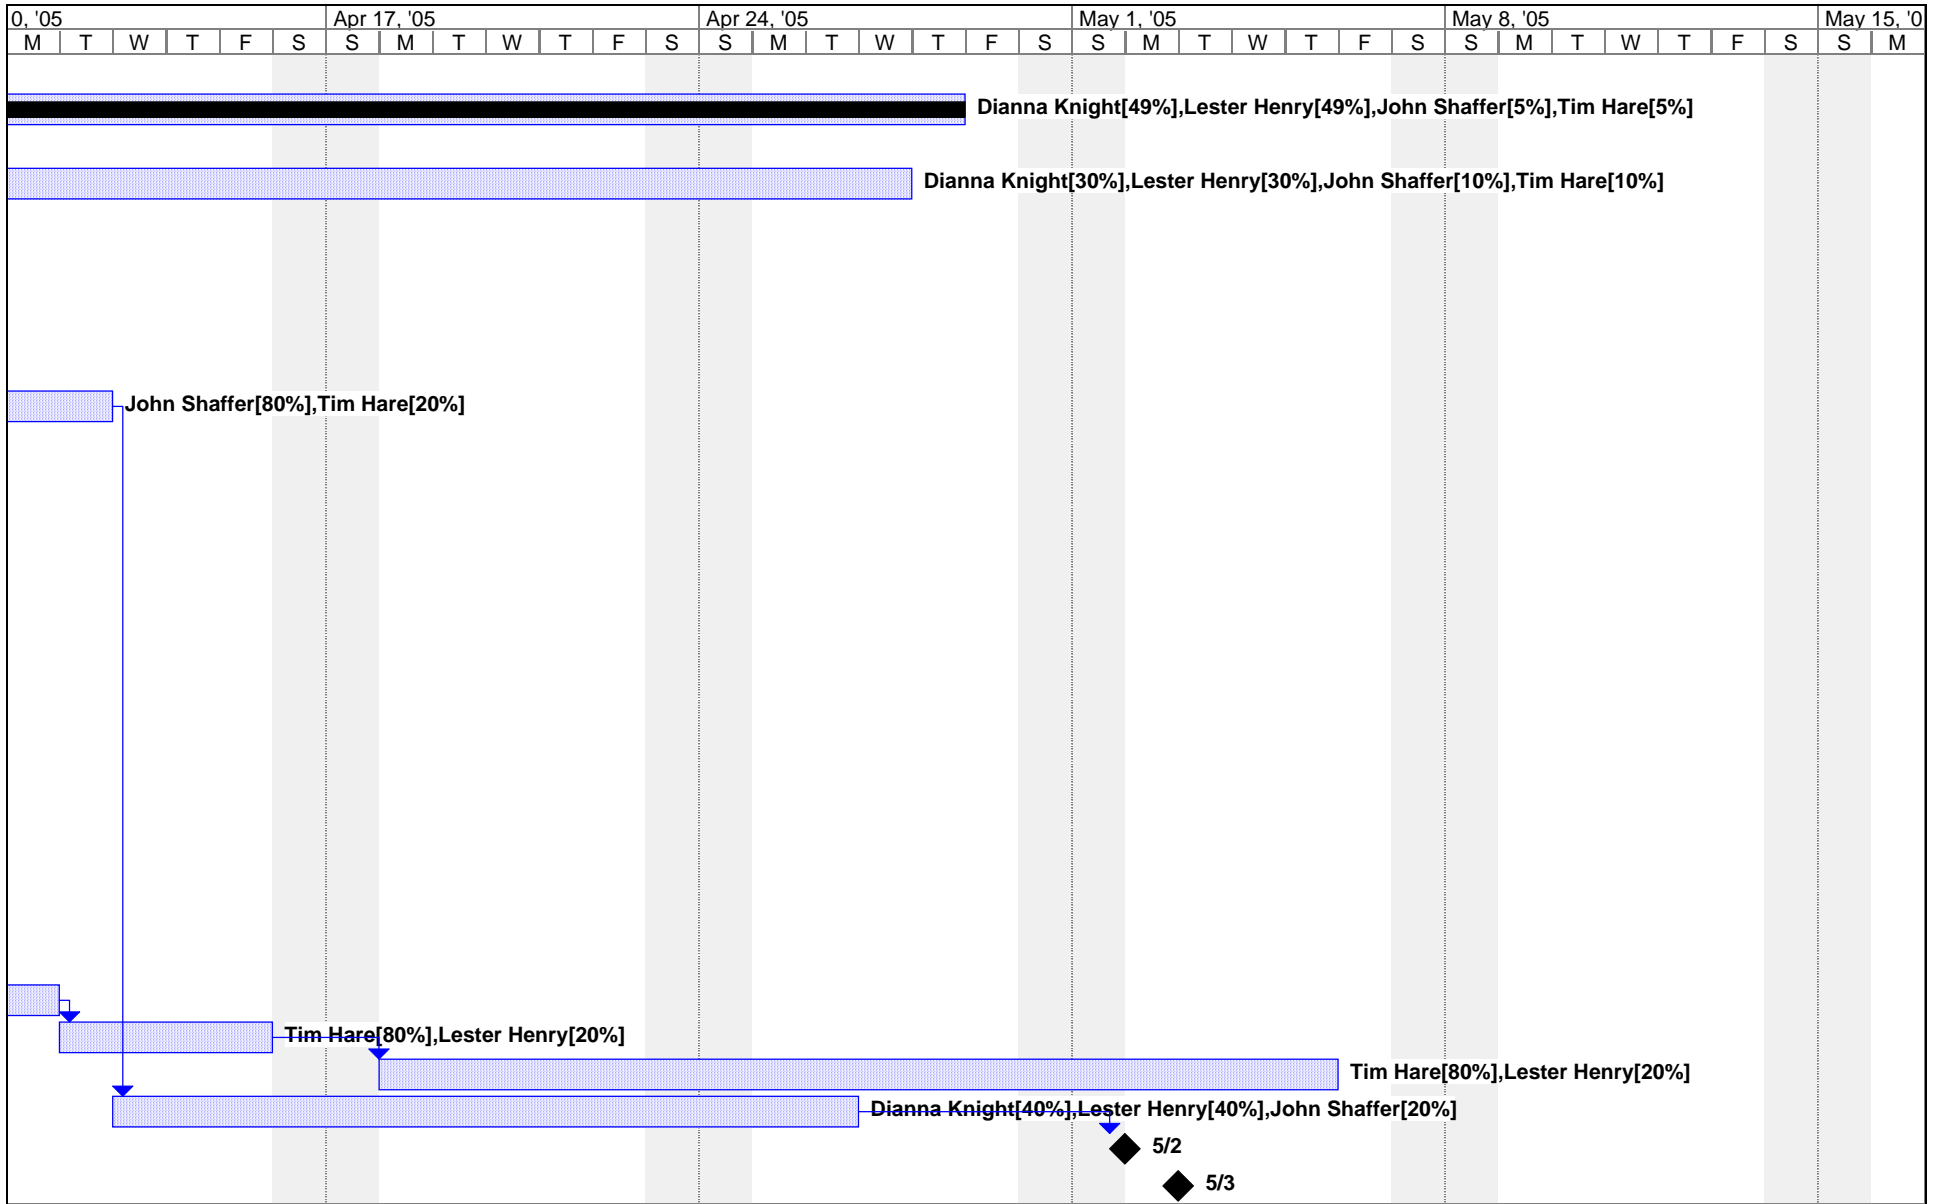

Project: GeorgiaPalm Date: Thu 3/3/05	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
